




August 10, 2021

Construction Update #4

- Detailed excavation will begin the week of August 9th, 2021.
- Large rakers will be installed on Saturday, August 14th. See details below.
 - Yorkville Avenue will be closed between Yonge Street and Bay Street from approximately 6:00am – 5:00pm.
 - Local traffic will be accommodated.
 - Public laneways with access to residential addresses will not be blocked and access to the firehall on Yorkville Avenue will be maintained.
 - 2 paid duty officers will be present to monitor traffic and pedestrian movement.

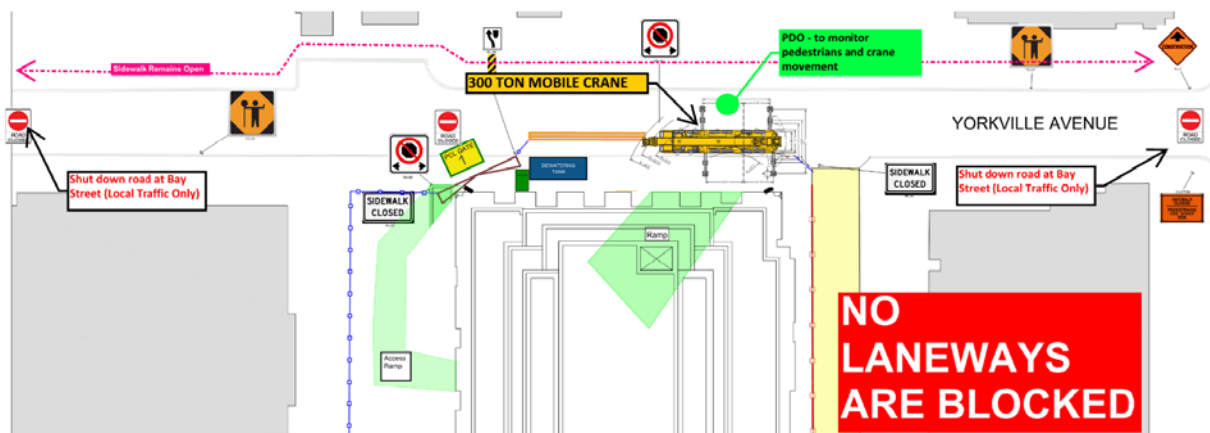

- Luffer crane will be installed in mid to late September, 2021. This will involve a temporary road closure. Details will be provided in a subsequent construction update.
- Raft Slab will be poured in mid-September, 2021. This will involve a temporary road closure. Details will be provided in a subsequent construction update.
- Covered scaffolding, in accordance with Ministry of Labor requirements, will be erected in the public laneways adjacent to the site in late August to early September.
- All contractors on site will continue adhere to the [new order](#) released by the Province of Ontario on April 7, 2020, which limits the City's authority to regulate noise in connection to construction and permits construction activity everyday between the hours of 6 a.m. and 10 p.m. for construction projects that are permitted to continue as part of the province's [list of essential workplaces](#). The order is in effect until October 7, 2021, unless revoked earlier by the Province.

See below high-level construction schedule.

Demolition Complete	October, 2020
Shoring pile drilling complete	February, 2020
Excavation and Tiebacks Start	March, 2021
Crane Erection & Below Grade Forming Start	September, 2021
Lateral Service Connection Installation	Fall, 2021
Above-Grade Forming	Spring, 2022
